



**IMEA Board of Directors Meeting  
TC-2 Presentation  
Oct 24, 2009**

## Major Milestones Achieved

- Overall 80% complete
- Boiler pressure parts installation 99% complete
- Boiler reheat hydro complete
- Final alignment of STG in progress
- Completed erection of DESP, PJFF, WFGD, and WESP
- Substation tie complete
- Ghent-Speed river crossing complete

## Non EPC Scope


- Completed installation of the RO, tripper room baghouses, new and refurbished service water system components, and new auxiliary boiler
- Completed the new fuel blending system
- Began installation of PRB dust control upgrades in the coal yard; consisting of new belt feeders, dustless transfer chutes, wash down system, painting of interior structures and equipment, and interior lighting upgrade

## Future Milestones

- Complete boiler hydro early Nov
- First fire on oil Jan 6, 2010
- Start steam blows Jan 7, 2010
- First fire on coal mid-Feb 2010
- First full load mid-Mar 2010
- Guaranteed Commercial Operation Jun 15, 2010 still intact

Peak Construction Workforce ~1,200

Estimated Jobhours ~4,000,000

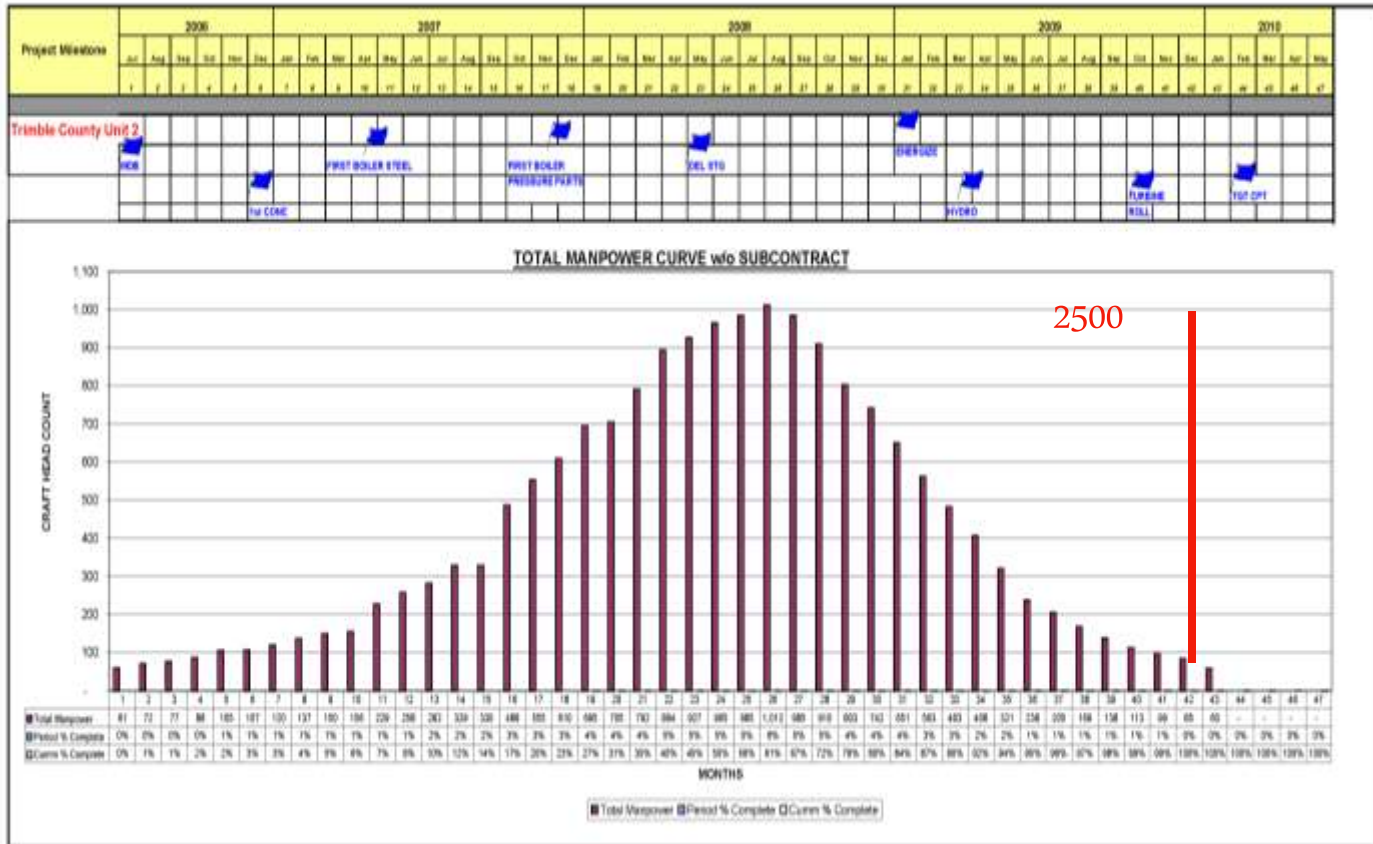

**AQCS Aerial**



**Turbine Aerial**



**Boiler**

